


DOWNTOWN STREETScape PHASE 1 CONSTRUCTION

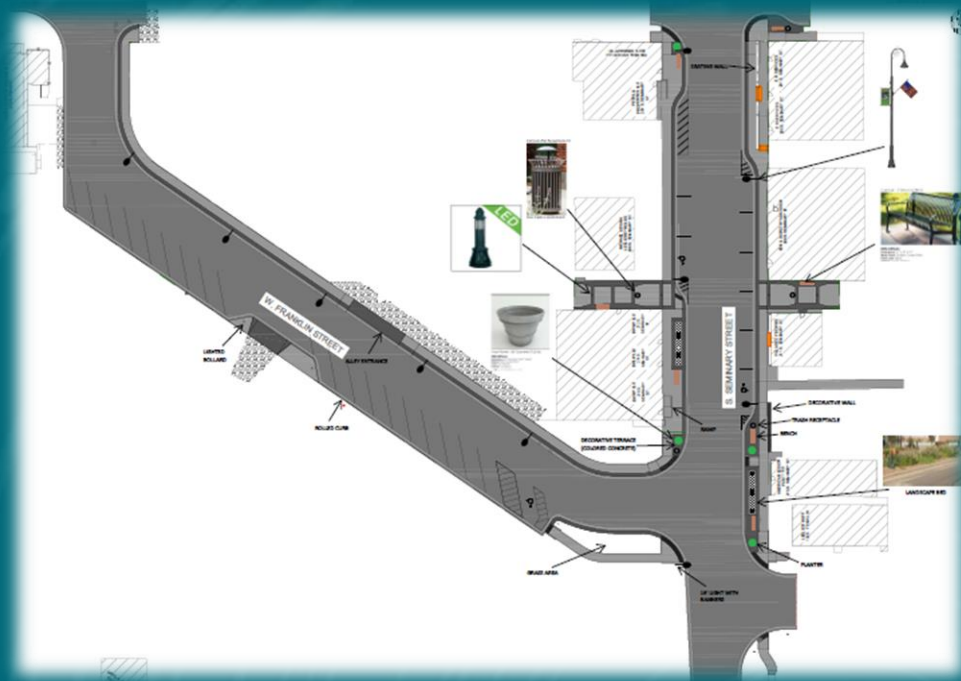

Public Information Meeting

May 27, 2025

STAGE 1 – W FRANKLIN ST

Wednesday May 28 to Friday June 27



1. Road closed until June 27
2. Some striping landscaping and cleanup done week after June 27
3. Alleys must remain accessible, from Seminary Street, to local businesses and residents.
4. Any work in this stage that affects traffic along Seminary Street shall be completed under daytime flagging operations.
5. Access shall be coordinated with local residents and the village throughout construction. Access shall be maintained to all businesses and residences at all times unless otherwise agreed to by the business/ property owner and approved by the engineer.

STAGE 2 – SEMINARY ST UTILITY WORK

Monday June 30 to Friday July 11



1. Close Seminary Street to traffic between Main Street and West Franklin Street. Detour traffic around the work area via West Franklin Street
2. A pedestrian access route shall be maintained throughout the duration of construction and sidewalk closed, and detour signs shall be utilized.
3. Access shall be coordinated with local residents and the village throughout construction. Access shall be maintained to all businesses and residences at all times unless Otherwise agreed to by the business/ property owner and approved by the engineer.

STAGE 3 – SEMINARY ST WESTSIDE

Monday July 14 to Friday July 25



1. A pedestrian access route shall be maintained throughout the duration of construction and sidewalk closed, and detour signs shall be utilized.
2. Temporary CL pavement striping and lane shift signs shall be required
3. Any work disrupting two-way traffic on Seminary Street shall be performed under daytime flagging operations
4. Parking along the east side of Seminary Street shall be maintained unless conditions become unsafe as determined by the Village and/or Engineer.

STAGE 4 – SEMINARY ST EASTSIDE

Monday July 28 to Friday August 8



1. A pedestrian access route shall be maintained throughout the duration of construction and sidewalk closed, and detour signs shall be utilized.
2. Temporary CL pavement striping and lane shift signs shall be required
3. Any work disrupting two-way traffic on Seminary Street shall be performed under daytime flagging operations
4. Parking along the west side of Seminary Street shall be maintained unless conditions become unsafe as determined by the Village and/or Engineer.

STAGE 5 – SEMINARY ST OVERLAY

Monday August 11 to Friday August 15



1. Stage 5 is to consist of final mill and overlay of seminary street and pavement marking painting.
2. Contractor shall perform mill and overlay of seminary street one lane at a time under flaggers. Contractor may suggest alternative method of traffic control, such as re-routing one direction of traffic around the work area via west franklin street. Any deviation from the plan must be approved by the engineer.
3. A pedestrian access route shall be maintained throughout the duration of construction and sidewalk closed, and detour signs shall be utilized.
4. Parking on Seminary Street will not be allowed during working hours.

Monday August 18 to Friday August 22

